SHEERID X LELAND

Layered support for the AI Acceleration Initiative.

October through February,
and the year that follows.

Leland

Agenda.

01	What we heard	AI Acceleration at SheerID
02	About Leland	An end-to-end AI enablement partner
03	Our solution	Enablement, dedicated support, and services
04	Commercial details	What it costs and what happens next

WHAT WE HEARD

An AI acceleration initiative over six months, the whole company activated by AKO in February.

This is every company's first AI transformation.

CHALLENGES

- **AI policy and risk.** Standardizing and unifying the company's AI policy ahead of mass adoption, avoiding costly economic, legal, and reputational risks.
- **Capability.** Make every role and level AI-first.
- **Resistance.** Change threatens identity. Will what people were good at still matter, and will the new job be as interesting?
- **L&D capacity.** Your strongest AI people have day jobs, and aren't always the strongest teachers.
- **Tracking impact.** Challenging to report ROI, progress, and impact to the board.

OUTCOMES

- **Output that scales without headcount.** ICs become managers of agents, scaling their impact.
- **An AI-first operating model.** Every role, process, and project is redesigned to be AI-first.
- **Company engagement.** A workforce that is excited about being AI-first, and feels prepared for the future rather than scared.
- **Customer alignment.** SheerID supports many of the most advanced AI companies. Keeping up with AI fluency keeps you aligned with them.
- **Clear ROI.** Board-ready reporting on the transformation and its impact.

ABOUT LELAND

An end-to-end AI enablement partner.

TRUSTED BY TEAMS AT   Morgan Stanley Salesforce Cisco Nomura Discover GitLab

3,500+
industry experts,
150+ pathways

4.99
average rating

7.5M+
people building careers
on Leland


Verizon. 13,000 employees supported through career transformation.
Governor's Office of Economic Development. Selected to support entrepreneurs statewide with AI enablement.

OUR SOLUTION

End-to-end layered support for AI acceleration.


AI Builder Foundations	Drive a 15% productivity improvement across all ~185 employees, and mitigate risk around data handling, shadow AI, and unverified output.
AI Builder Program	Phased enablement in waves: SLT and ELT first, squads in roadmap order, then company-wide at AKO.
1:1 support in your function	Each executive and cluster lead paired with an AI-first leader who has run this inside their own function.
AI engineering and AI services	10 hours a month from kickoff, drawn on demand for AI engineering or AI leadership support.
Workshops and the AI Innovation Sprint	Three executive workshops built on your context, and the AI Innovation Sprint ahead of AKO so squads walk in with working agents to demo.

An 18-month roadmap: October 1, 2026 to March 31, 2028.

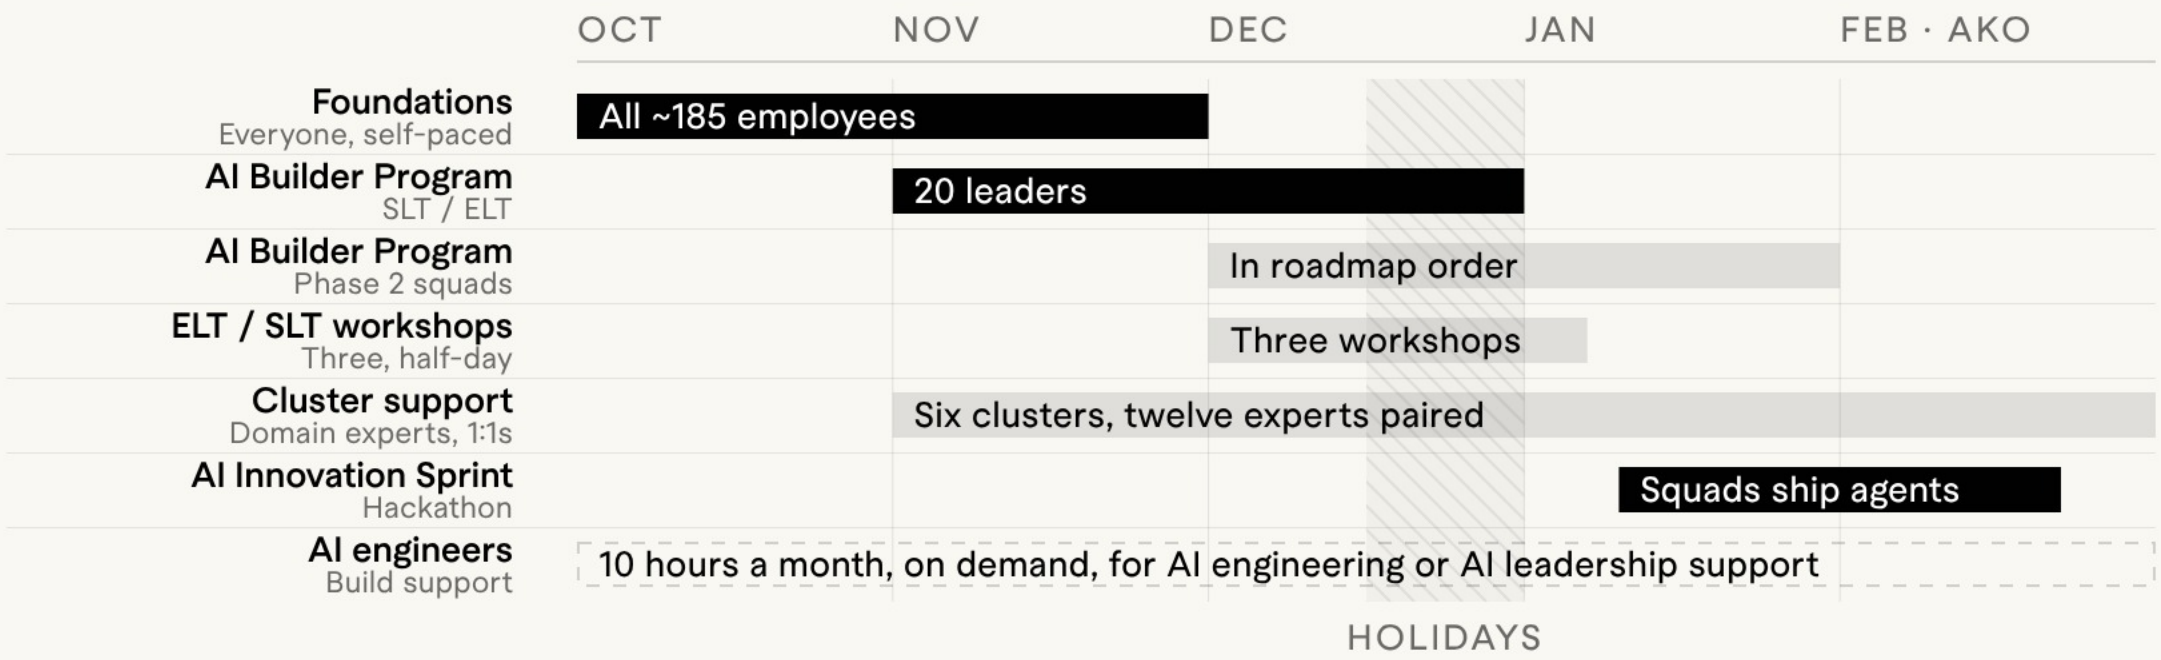

Why October. A November start runs into the holidays, which slow progress and momentum. Driving baseline fluency in October, ahead of the phased enablement waves, has produced the strongest adoption while mitigating near-term compliance, security, and reputational risks.

The roadmap continues: February 2027 onward.

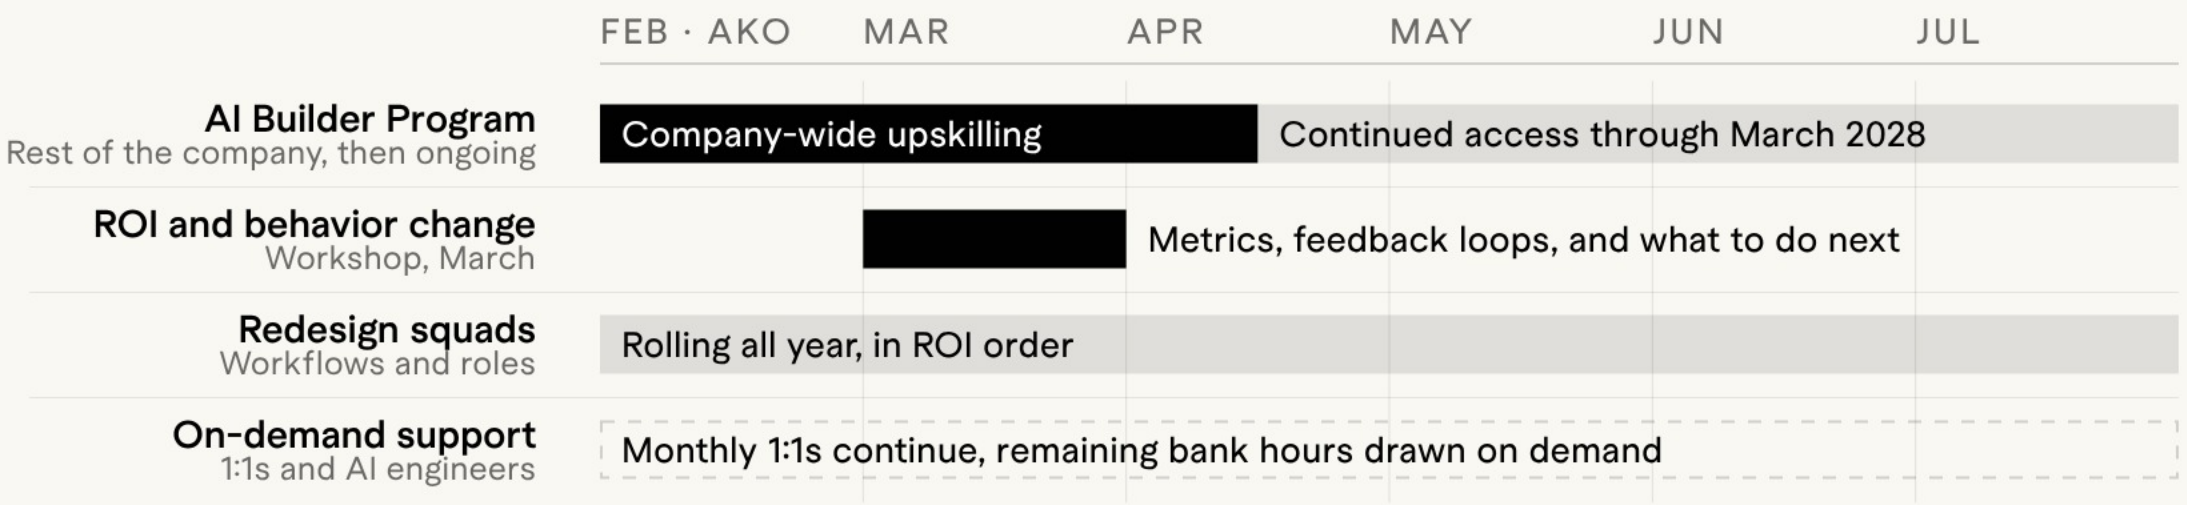

Continued access

Employees retain access to the AI Builder Program and its updated curriculum through March 2028, so skills compound as models change.

On-demand support

The AIA, squad leaders, and executives keep 1:1 support from domain experts, with AI engineers on call for technical help.

ROI analysis

Metrics, reporting, and feedback loops to track ROI and flag opportunities for cost savings, process improvement, and continued enablement.

Leland

18 months of support for AI Acceleration.

AI enablement for every employee

- Baseline fluency for all ~185 employees with Foundations
- The full AI Builder Program for all ~200 employees, delivered in waves, so every team builds agents, automations, and tools for their own roles
- Custom curriculum on SheerID's data privacy, standards, and tool-specific nuances
- 18 months of curriculum access for all ~200 employees

Dedicated support from AI-first leaders

- A domain expert paired with every functional cluster and lead
- Six months of FY27 support from domain experts
- A 60-hour bank from kickoff, 10 hours a month, drawn on demand for AI engineering or AI leadership support
- Analytics on engagement, project builds, and skill improvement

Custom workshops and curriculum, built for SheerID

- Three executive workshops: reclaim their own time, lead the change with their teams, prove ROI to the board
- The AI Innovation Sprint (Hackathon) ahead of AKO
- ROI Analysis and Behavior Change Workshop in March

COMMERCIAL DETAILS

18 months of dedicated support for the AIA.

FULL SOLUTION

$250,000

October 1, 2026 through March 31, 2028 · Kickoff October 1

- Scalable, impactful AI enablement for every employee
- Avoid costly mistakes with dedicated support from AI-first leaders
- Address executive priorities and accelerate time-to-value with custom workshops and innovation sprints

Two ways to begin.

OPTION 1 · FULL PARTNERSHIP

$190,000

Company-wide AI Foundations with your policy content, data-privacy design group, and board reporting

The full AI Builder Program for every employee: SLT / ELT first, then squads in roadmap order, then company-wide

Three executive workshops and the AI Innovation Sprint ahead of AKO

Domain experts across all six functional clusters, plus monthly 1:1s for cluster leads

A 60-hour bank from kickoff, 10 hours a month, drawn on demand for AI engineering or AI leadership support

18 months of curriculum access for all ~200 employees

Signed by September 18 · kickoff October 1

OPTION 2
FOUNDATIONS PILOT AND DESIGN PARTNER

$55,000

Company-wide AI Foundations for all 185

Your AI policy and data-classification content woven in

Data privacy and guardrails designed with a five-person group before launch

Board-ready reporting pack

Everything in Option 1 priced and dated, credited in full if you continue

Signed by September 30 · kickoff October 10

List price for this scope is $250,000. The partnership is $190,000, 24% below list.

Leland

NEXT STEPS

From here to kickoff.

SEPT 7-8	SEPT 9-11	SEPT 14-15	SEPT 18	OCT 1
Solution refinement with Laura	Onsite with the AIA and leadership team	Finalized SOW	Contracting complete	**Kick-off**

Leland

Appendix.

Foundations, the five levels, the bench, and how progress gets measured.

Near-term productivity, while mitigating risks.

Everyone, self-paced, about seven hours

- **See the potential.** Where AI actually fits their own job, and what it can do beyond search.
- **Use it effectively.** Giving AI real context, staying organized, and getting output worth keeping.
- **Use it responsibly.** Security, honesty about what AI produces, and control of what it costs.

Four live sessions over two weeks

- Deliver a working product, end to end
- Automate communication in your voice, analyze data, and create presentations with AI
- Design role-specific skills
- Demo day and certificates. Access included for the SLT / ELT and every wave that follows

Custom to SheerID

- **AI policy reinforcement.** Your AI policy and data classification, taught in the same round, so level set and policy launch are one motion.
- **Data-privacy guardrails.** A five-person design group goes first, so data boundaries are set before the company-wide launch.
- **Board-ready reporting.** Baseline and post competency, completion, compliance, and adoption, reported to the AI Acceleration team each cohort.

AI BUILDER PROGRAM

Empower every team to be an AI Builder.

Five levels of enablement, from first build to an orchestration layer, designed by AI experts for knowledge workers, with a year of curriculum updates as models change.
One matched expert per functional cluster, plus a monthly 1:1 with every cluster lead.

01	02	03	04	05
Use AI to 10x your impact	Build complex agentic workflows	Create autonomous agents	Build your agent workforce	Design your AI orchestration layer

Level one clears your infrastructure gate today. The deeper levels unlock as systems connect. The program moves at the speed of your infrastructure, not our calendar.

Leland

Domain experts who have run this inside their own function.

Go-to-Market

- **Tara C.** SVP Marketing; VP MktOps, AppFolio
- **Albert C.** P&G, Google, Meta

Finance

- **Elyse R.** Deloitte, KPMG, PwC; Copilot to 5,000+
- **Juston B.** Sr Financial Analyst, Google; MS in AI

Info Security

- **Atul T.** IBM, HCLTech; security and governance
- **Frances C.** Slack, JupiterOne; compliance

Product

- **Charles T.** Head of AI Product, Intuit
- **Dessy K.** Ex-TikTok Head of Product

Marketing

- **Nasiim S.** Meta, Microsoft; AI operating systems
- **Rachael D.** Airbnb, Meta, eBay; lifecycle AI

People and Leadership

- **Cheryl R.** VP of AI Transformation; ICF-certified
- **Mike H.** Stanford GSB; leading teams in the AI era

Each cluster lead keeps a monthly 1:1 through February, and six months further into FY27.

REPORTING

How progress gets measured.

Fluency improvement

Before the program, participants are surveyed to baseline current AI competency. After, a follow-up survey gauges the lift, person by person.

Engagement and accountability

Attendance, recording views, and completion tracked throughout and reported to the AI Acceleration team, so you can see who is progressing and who needs support.

Business impact

Agents and automations built inside the program, counted per cohort, then function-specific builds from the Sprint, showcased at AKO.

These become the first numbers behind the ROI gates in your own plan, and the progress report your board is expecting.
